

SREEROSH ORCHARD

WORK PROGRESS
APRIL 2026



SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:30-04-2026

	RETAINING WALL	VILLA # 01	VILLA # 02	VILLA # 03	VILLA # 04	VILLA # 05	VILLA # 06	VILLA # 07	VILLA # 08	VILLA # 09	VILLA # 10	VILLA # 11	VILLA # 12
Level Pad Fixing													
Ground floor													
First floor													
Plastering													
Ground floor													
First floor													
Floor PCC													
Ground floor													
Water Proofing													
Toilets													
Roof													
Floor Tiling													
Ground floor													
First floor													
Wall tiling													
Ground floor													
First floor													
External plaster													
Ground floor													
Painting													
Internal													
External													
Doors & Windows													
Doors													
Windows													
Roof tiling													

CIVIL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

	VILLA # 25	VILLA # 26	VILLA # 27	VILLA # 28	VILLA # 29	VILLA # 30	VILLA # 31	VILLA # 32	VILLA # 33	VILLA # 34	VILLA # 35	VILLA # 36
Level Pad Fixing												
Ground floor	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green		Green
First floor	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green		Green
Plastering												
Ground floor	Green		Green	Green	Green	Yellow	Green			Green		Green
First floor	Green		Green	Green	Green	Yellow	Green			Green		Green
Floor PCC	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green
Water Proofing												
Toilets			Green	Green	Green							
Roof												
Floor Tiling												
Ground floor												
First floor												
Wall tiling												
Ground floor												
First floor												
External plaster	Yellow		Green	Green	Yellow					Yellow		
Painting												
Internal			Yellow	Yellow								
External												
Doors & Windows												
Doors												
Windows												

VILLA # 15


CIVIL WORKS

INDEX	
Green	COMPLETED
Yellow	PROGRESS
Blue	DATE
	PLANNED FINISHE DATE

Sloped Roof						
LS above Slab/ Level						
FF Roof Slab (2nd F)						
LS Above Lintel						
Lintel Beam, Sunshade						
LS above Slab upto Lintel						
GF Roof Slab (1st F)						
LS Above Lintel						
Lintel Beam, Sunshade						
Stair - upto Landing						
LS Above PB						
Grade slab						
Earth Filling		VILLA #				
Plinth Beam		VILLA # 23				
Foundation / Basement		VILLA # 23				
Excavation			12.12.2025			
RR/ LS Partition	RR	RR	LS	RR	LS	RR
	VILLA # 20	VILLA # 23	VILLA # 24	VILLA # 21	VILLA # 22	
	RR	RR		RR		
	VILLA # 19	VILLA # 25		VILLA # 20		

INDEX

DATE	COMPLETED
	PROGRESS
DATE	PLANNED START DATE
	NOT COMMENCED
	NOT APPLICSBLE
	SCOPE OF KRISHNA BUILDERS

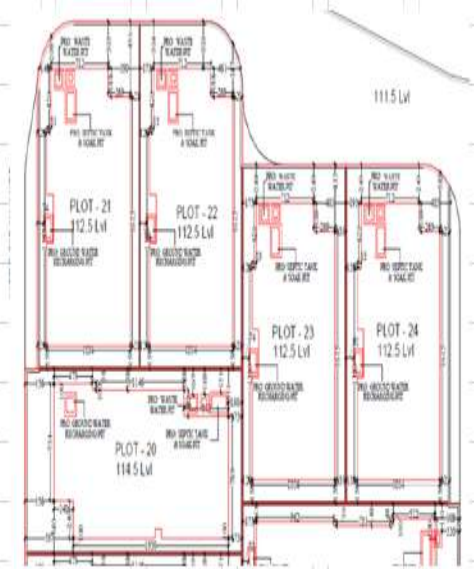

CIVIL WORKS

SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT -CLUB HOUSE

DATE: 30-04-2026

Column No.	1	2	3	4	5	6	7	8	9	11	12	13	10	14	15	16	19	22	17	18	20	21
Stair room Slab																						
Laterite masonry at B1 Level	06-03-2026		60% Completed																			
Laterite masonry at B2 Level	10-04-2026		40% Completed																			
Laterite masonry at GF Level																						
Parapet on roof																						
Parapet on Head room slab																						
Plastering in B1 level																						
Plastering in B2 level																						
Plastering in GF level																						
Parapet Plastering																						
Plumbing in Toilets																						
Plumbing in Kitchen																						
Waterproofing																						
Tiling B1																						
Plastering of Swimming pool																						
Tiling B2																						
Tiling GF																						

CLUB HOUSE CIVIL WORKS




VILLA # 01





VILLA # 02





VILLA # 03





VILLA # 04





VILLA # 05





VILLA # 06






VILLA # 07



VILLA # 08



VILLA # 09





VILLA # 10



VILLA # 11





VILLA # 12



VILLA # 13






LC-280925

VILLA # 14





VILLA # 15





VILLA # 16





VILLA # 17





VILLA # 18





VILLA # 19






VILLA # 20





VILLA # 21





VILLA # 22





VILLA # 23





VILLA # 24





VILLA # 25

VILLA-25



VILLA # 26



VILLA # 27





VILLA # 28





VILLA # 29





VILLA # 30





VILLA # 31





VILLA # 32



VILLA # 33






VILLA # 34






VILLA # 35





VILLA # 36

VILLA-36





VILLA # 37



VILLA # 38



CLUB HOUSE





**Water proofing in
toilets**



Internal Rendering





UPVC Windows





