

SREEROSH ORCHARD

WORK PROGRESS
DECEMBER 2025



WORK PROGRESS REPORT

Level Pad Fixing													
Ground floor						13.12.2025	22-12.2025	25.12.2025	26.12.2025				
First floor					09.12.2025	13.12.2025	22-12.2025	25.12.2025	26.12.2025				
Plastering													
Ground floor		29.12.2025	30.12.2025	19.12.2025									
First floor		22.12.2025	29.12.2025										
Floor PCC													
Water Proofing													
Toilets													
Roof													
Floor Tiling													
Ground floor													
First floor													
Wall tiling													
Ground floor													
First floor													
External plaster				10.12.2025									
Painting													
Internal													
External													
Doors & Windows													
Doors													
Windows													
	VILLA # 01	VILLA # 02	VILLA # 03	VILLA # 04	VILLA # 05	VILLA # 06	VILLA # 07	VILLA # 08	VILLA # 09	VILLA # 10	VILLA # 11	VILLA # 12	

RETAINING WALL

CIVIL WORKS

INDEX				
DATE	COMPLETED			
COMPLETE BY	PROGRESS			
DATE	PLANNED START DATE			
	NOT COMMENCED			

WORK PROGRESS REPORT

Level Pad Fixing													
Ground floor							13.12.2025						
First floor							13.12.2025						
Plastering													
Ground floor								10.12.2025		29.12.2025	15.12.2025		
First floor										31.12.2025	22.12.2025		
Floor PCC													
Water Proofing													
Toilets													
Roof													
Floor Tiling													
Ground floor													
First floor													
Wall tiling													
Ground floor													
First floor													
External plaster								24.12.2025					
Painting													
Internal													
External													
Doors & Windows													
Doors													
Windows													
	VILLA # 13	VILLA # 14	VILLA # 15	VILLA # 16	VILLA # 17	VILLA # 18	VILLA # 19	VILLA # 25	VILLA # 26	VILLA # 27	VILLA # 28	VILLA # 29	

INDEX			
DATE	COMPLETED		
COMPLETE BY	PROGRESS		
DATE	PLANNED START DATE		
	NOT COMMENCED		

CIVIL WORKS

CIVIL WORKS

INDEX			
DATE	COMPLETED		
COMPLETE BY	PROGRESS		
DATE	PLANNED START DATE		
	NOT COMMENCED		

WORK PROGRESS REPORT

[illegible]

ELECTRICAL WORKS

INDEX			
DATE	COMPLETED		
COMPLETE BY	PROGRESS		
DATE	PLANNED START DATE		
	NOT COMMENCED		

WORK PROGRESS REPORT

[illegible]

ELECTRICAL WORKS

INDEX			
DATE	COMPLETED		
COMPLETE BY	PROGRESS		
DATE	PLANNED START DATE		
	NOT COMMENCED		

WORK PROGRESS REPORT

[illegible]

ELECTRICAL WORKS

INDEX			
DATE	COMPLETED		
COMPLETE BY	PROGRESS		
DATE	PLANNED START DATE		
	NOT COMMENCED		


WORK PROGRESS REPORT					
Wall Chasing					
Ground floor					
First floor					
Box fixing					
Ground floor					
First floor					
Conduit fixing					
Ground floor					
First floor					
Wiring					
Ground floor					
First floor					
Switches and sockets					
Ground floor					
First floor					
DB Dressing					
VILLA #27					
		VILLA #36		VILLA # 37	VILLA # 38

ELECTRICAL WORKS

INDEX			
DATE	COMPLETED		
COMPLETE BY	PROGRESS		
DATE	PLANNED START DATE		
	NOT COMMENCED		

WORK PROGRESS REPORT

Sloped Roof							
LS above Slab/ Level							
FF Roof Slab (2nd F)							
LS Above Lintel							
Lintel Beam, Sunshade							
LS above Slab upto Lintel							
GF Roof Slab (1st F)							
LS Above Lintel							
Lintel Beam, Sunshade							
Stair - upto Landing							
LS Above PB							
Earth Filling							
Plinth Beam							
Foundation / Basement							
Excavation							
RR/ LS Partition							
	VILLA # 20	VILLA # 23	VILLA # 24	VILLA # 21	VILLA # 22		
	RR	RR	RR	RR	RR		
	VILLA # 19	VILLA # 25		VILLA # 20			

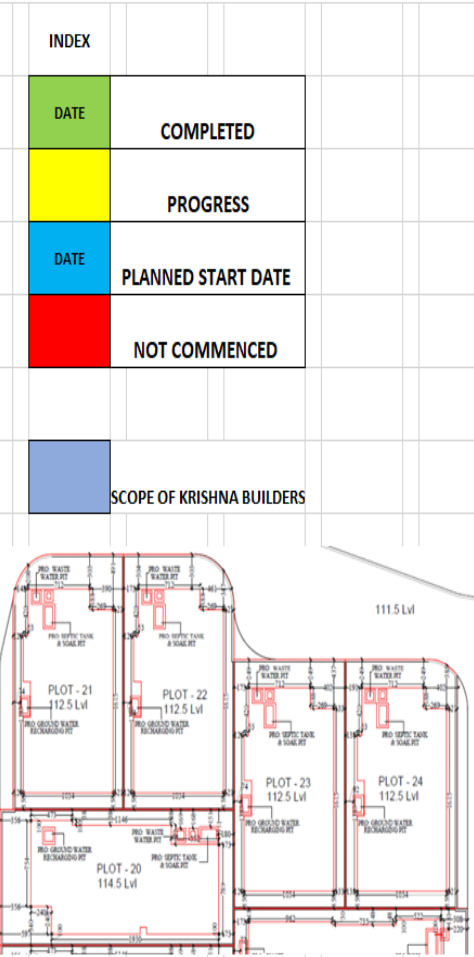

CIVIL WORKS

WORK PROGRESS REPORT

[illegible]

CLUB HOUSE CIVIL WORKS



VILLA # 01



VILLA # 02



VILLA # 03



VILLA # 04



VILLA # 05



VILLA # 06



VILLA # 07



VILLA # 08



VILLA # 09



VILLA # 10



VILLA # 11



VILLA # 12



VILLA # 13



VILLA # 14



VILLA # 15



VILLA # 16



VILLA # 17



VILLA # 18



VILLA # 19



VILLA # 20



VILLA # 21



VILLA # 22



VILLA # 23



VILLA # 24



VILLA # 25



VILLA # 26



VILLA # 27



VILLA # 28



VILLA # 29



VILLA # 30



VILLA # 31





VILLA # 32



VILLA # 33




VILLA # 34



VILLA # 35



VILLA # 36





VILLA # 37



VILLA # 38




CLUB HOUSE




PLUMBING WORKS
VILLA # 01



INTERNAL RENDERING VILLA # 02









RENDERING



EXTERNAL PLASTER



Electrical conduit laying



Electrical box fixing



