

SREEROSH ORCHARD

WORK PROGRESS
MARCH 2026



SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:31-03-2026

	VILLA # 01	VILLA # 02	VILLA # 03	VILLA # 04	VILLA # 05	VILLA # 06	VILLA # 07	VILLA # 08	VILLA # 09	VILLA # 10	VILLA # 11	VILLA # 12
Level Pad Fixing												
Ground floor	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green
First floor	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green
Plastering												
Ground floor	Green	Green	Yellow	Yellow		06-04-2026	06-04-2026					Yellow
First floor	Green	Green	Yellow			06-04-2026	06-04-2026					Yellow
Floor PCC												
Ground floor	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green
First floor	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green	Green
Water Proofing												
Toilets	Green	Green	Yellow									
Roof	Green	Green	Yellow	Yellow								
Floor Tiling												
Ground floor	Green											
First floor	Yellow											
Wall tiling												
Ground floor	Yellow											
First floor	Yellow											
External plaster												
Ground floor	Green	Green	Yellow	Yellow								
First floor	Green	Green	Yellow	Yellow								
Painting												
Internal	Yellow	Yellow										
External	Yellow											
Doors & Windows												
Doors	Yellow											
Windows	Yellow											

RETAINING WALL

RETAINING WALL

CIVIL WORKS

INDEX	
Green	COMPLETED
Yellow	PROGRESS
Blue	DATE
	PLANNED FINISHE DATE

Level Pad Fixing												
Ground floor	■	■	■	■	■	■	■	■	■	■		■
First floor	■	■	■	■	■	■	■	■	■	■		■
Plastering												
Ground floor	■		■	■	■		■			■		■
First floor	■		■	■	■		■			■		■
Floor PCC												
Water Proofing												
Toilets												
Roof												
Floor Tiling												
Ground floor												
First floor												
Wall tiling												
Ground floor												
First floor												
External plaster	■		■	■	■		■					
Painting												
Internal			■	■								
External												
Doors & Windows												
Doors												
Windows												
VILLA # 15	VILLA # 25	VILLA # 26	VILLA # 27	VILLA # 28	VILLA # 29	VILLA # 30	VILLA # 31	VILLA # 32	VILLA # 33	VILLA # 34	VILLA # 35	VILLA # 36

CIVIL WORKS

INDEX	
■	COMPLETED
■	PROGRESS
■	PLANNED FINISHE DATE

SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:31-03-2026

Level Pad Fixing					
Ground floor					
First floor					
Plastering					
Ground floor					
First floor					
Floor PCC					
Water Proofing					
Toilets					
Roof					
Floor Tiling					
Ground floor					
First floor					
Wall tiling					
Ground floor					
First floor					
External plaster					
Painting					
Internal					
External					
Doors & Windows					
Doors					
Windows					
	VILLA # 27				
		VILLA # 37		VILLA # 38	

CIVIL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE


SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:01-03-2026 to 31-03-2026

		DATE : 06-04-2026	DATE 12-03-2026		
Sloped Roof					
LS above Slab/ Level					
FF Roof Slab (2nd F)					
LS Above Lintel					
Lintel Beam, Sunshade					
LS above Slab upto Lintel					
GF Roof Slab (1st F)					
LS Above Lintel					
Lintel Beam, Sunshade					
Stair - upto Landing					
LS Above PB					
Grade slab					
Earth Filling					
Plinth Beam					
Foundation / Basement					
Excavation					
RR/ LS Partition					
	VILLA # 20	VILLA # 23	VILLA # 24	VILLA # 21	VILLA # 22
	RR	RR		RR	
	VILLA # 19	VILLA # 25		VILLA # 20	

INDEX	
	COMPLETED
	PROGRESS
	DATE
	PLANNED FINISHE DATE
	NOT COMMENCED
	NOT APPLICSBLE
	SCOPE OF KRISHNA BUILDERS

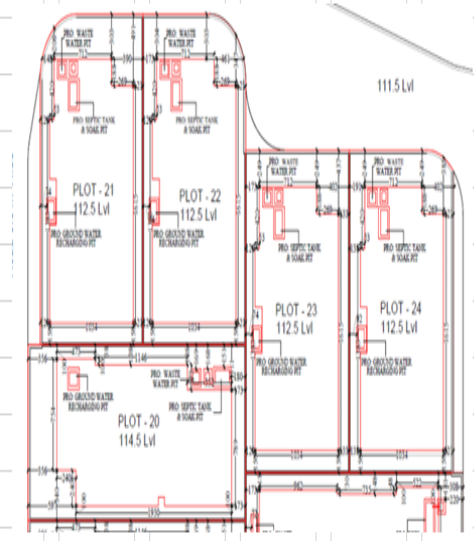

CIVIL WORKS

M/s ALOUJ ASSOCIATES

M/s KRISHNA BUILDERS

SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT -CLUB HOUSE

DATE: 01-03-2026 to 31-03-2026

Column No.	1	2	3	4	5	6	7	8	9	11	12	13	10	14	15	16	19	22	17	18	20	21
Stair room Slab																						
Laterite masonry at B1 Level																						
Laterite masonry at B2 Level																						
Laterite masonry at GF Level																						
Parapet on roof																						
Parapet on Head room slab																						
Plastering in B1 level																						
Plastering in B2 level																						
Plastering in GF level																						
Parapet Plastering																						
Plumbing in Toilets																						
Plumbing in Kitchen																						
Waterproofing																						
Tiling B1																						
Plastering of Swimming pool																						
Tiling B2																						
Tiling GF																						
Retaining wall plaster																						

CLUB HOUSE CIVIL WORKS





VILLA # 01





VILLA # 02





VILLA # 03






VILLA # 04





VILLA # 05





VILLA # 06



VILLA # 07



VILLA # 08



1110-17-9-25

1/9

VILLA # 09





VILLA # 10





VILLA # 11






LC-25-09-25

VILLA # 12






VILLA # 13






LC-28/09-25

VILLA # 14





VILLA # 15






VILLA # 16





VILLA # 17






VILLA # 18






VILLA # 19





VILLA # 20





VILLA # 21





VILLA # 22





VILLA # 23





VILLA # 24





VILLA # 25






VILLA # 26





VILLA # 27





VILLA # 28





VILLA # 29





VILLA # 30





VILLA # 31






VILLA # 32





VILLA # 33





VILLA # 34






VILLA # 35





VILLA # 36





VILLA # 37






VILLA # 38





CLUB HOUSE





Putty application on walls



Internal Plumbing lines





Electrical Conduiting





