


SREEROSH ICON
PROGRESS REPORT APRIL 2026



PILING WORK PROGRESS

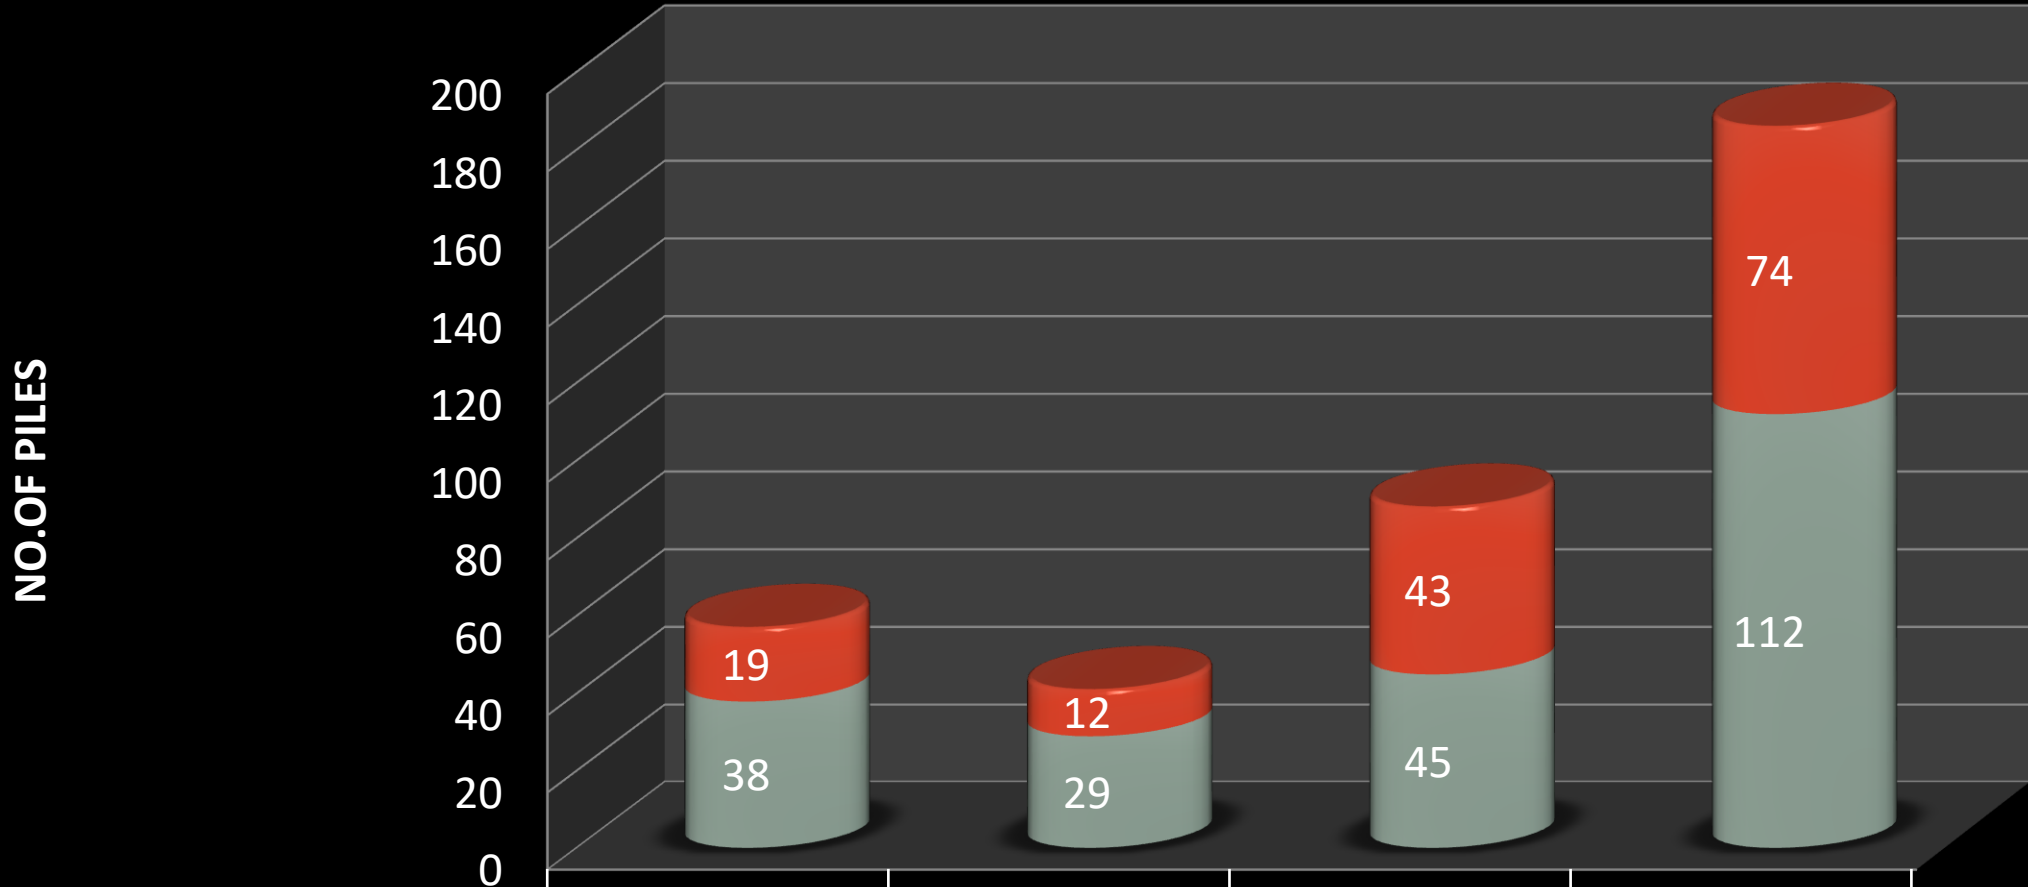

■ BALANCE TO COMPLETE

■ COMPLETED

800mm

900mm

1000mm

TOTAL

19

12

43

74

38

29

45

112

PROGRESS PHOTOS



PILING WORKS



PILING WORKS



PILE CASTING



2026 05 05 10:27

REINFORCEMENT CAGE FABRICATION

THANK YOU
