

SREEROSH ORCHARD

WORK PROGRESS
JULY 2026



SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:31-07-2026

	VILLA # 01	VILLA # 02	VILLA # 03	VILLA # 04	VILLA # 05	VILLA # 06	VILLA # 07	VILLA # 08	VILLA # 09	VILLA # 10	VILLA # 11	VILLA # 12
Level Pad Fixing												
Ground floor												
First floor												
Plastering												
Ground floor												
First floor												
Floor PCC												
Water Proofing												
Toilets												
Roof												
Floor Tiling												
Ground floor												
First floor												
Wall tiling												
Ground floor												
First floor												
External plaster												
Painting												
Internal												
External												
Doors & Windows												
Doors												
Windows												
Roof tiling												

RETAINING WALL

RETAINING WALL

CIVIL WORKS

INDEX

	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:31-07-2026

Level Pad Fixing													
Ground floor													
First floor													
Plastering													
Ground floor													
First floor													
Floor PCC													
Water Proofing													
Toilets													
Roof													
Floor Tiling													
Ground floor													
First floor													
Wall tiling													
Ground floor													
First floor													
External plaster													
Painting													
Internal													
External													

INTERNAL ROAD

CIVIL WORKS

INDEX

	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

DATE:31-07-2026

CIVIL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT DATE:31-07-2026

		VILLA # 37	VILLA # 38			
Level Pad Fixing						
Ground floor						
First floor						
Plastering						
Ground floor						
First floor						
Floor PCC						
Water Proofing						
Toilets						
Roof						
Floor Tiling						
Ground floor						
First floor						
Wall tiling						
Ground floor						
First floor						
External plaster						
Painting						
Internal						
External						
Doors & Windows						
Doors						
Windows						
		VILLA # 37	VILLA # 38			

VILLA # 27

CIVIL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

DATE:31-07-2026

ELECTRICAL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:31-07-2026

[illegible]

ELECTRICAL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

SREEROSH ORCHARD, KOYYODE - KANNUR

WORK PROGRESS REPORT

DATE:31-07-2026

[illegible]

ELECTRICAL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

DATE:31-07-2026

ELECTRICAL WORKS

INDEX	
	COMPLETED
	PROGRESS
DATE	PLANNED FINISHE DATE

Column No.	1	2	3	4	5	6	7	8	9	11	12	13	10	14	15	16	19	22	17	18	20	21	
Stair room Slab																							
Laterite masonry at B1 Level	60% Completed																						
Laterite masonry at B2 Level	40% Completed																						
Laterite masonry at GF Level	10% Completed																						
Parapet on roof																							
Parapet on Head room slab																							
Plastering in B1 level																							
Plastering in B2 level																							
Plastering in GF level																							
Parapet Plastering																							
Plumbing in Toilets																							
Plumbing in Kitchen																							
Waterproofing																							
Tiling B1																							
Plastering of Swimming pool																							
Tiling B2																							
Tiling GF																							
Retaining wall plaster																							

CLUB HOUSE CIVIL WORKS



VILLA # 01



VILLA # 02



VILLA # 03



VILLA # 04



VILLA # 05



VILLA # 06



VILLA # 07



VILLA # 08



VILLA # 09



VILLA # 10



VILLA # 11



VILLA # 12



VILLA # 13



VILLA # 14



VILLA # 15



VILLA # 16



VILLA # 17



VILLA # 18



VILLA # 19



VILLA # 20



VILLA # 21



VILLA # 22



VILLA # 23



VILLA # 24



VILLA # 25



VILLA # 26



VILLA # 27



VILLA # 28



VILLA # 29



VILLA # 30



VILLA # 31



VILLA # 32



VILLA # 33




VILLA # 34



VILLA # 35



VILLA # 36





VILLA # 37



VILLA # 38






CLUB HOUSE



Rendering

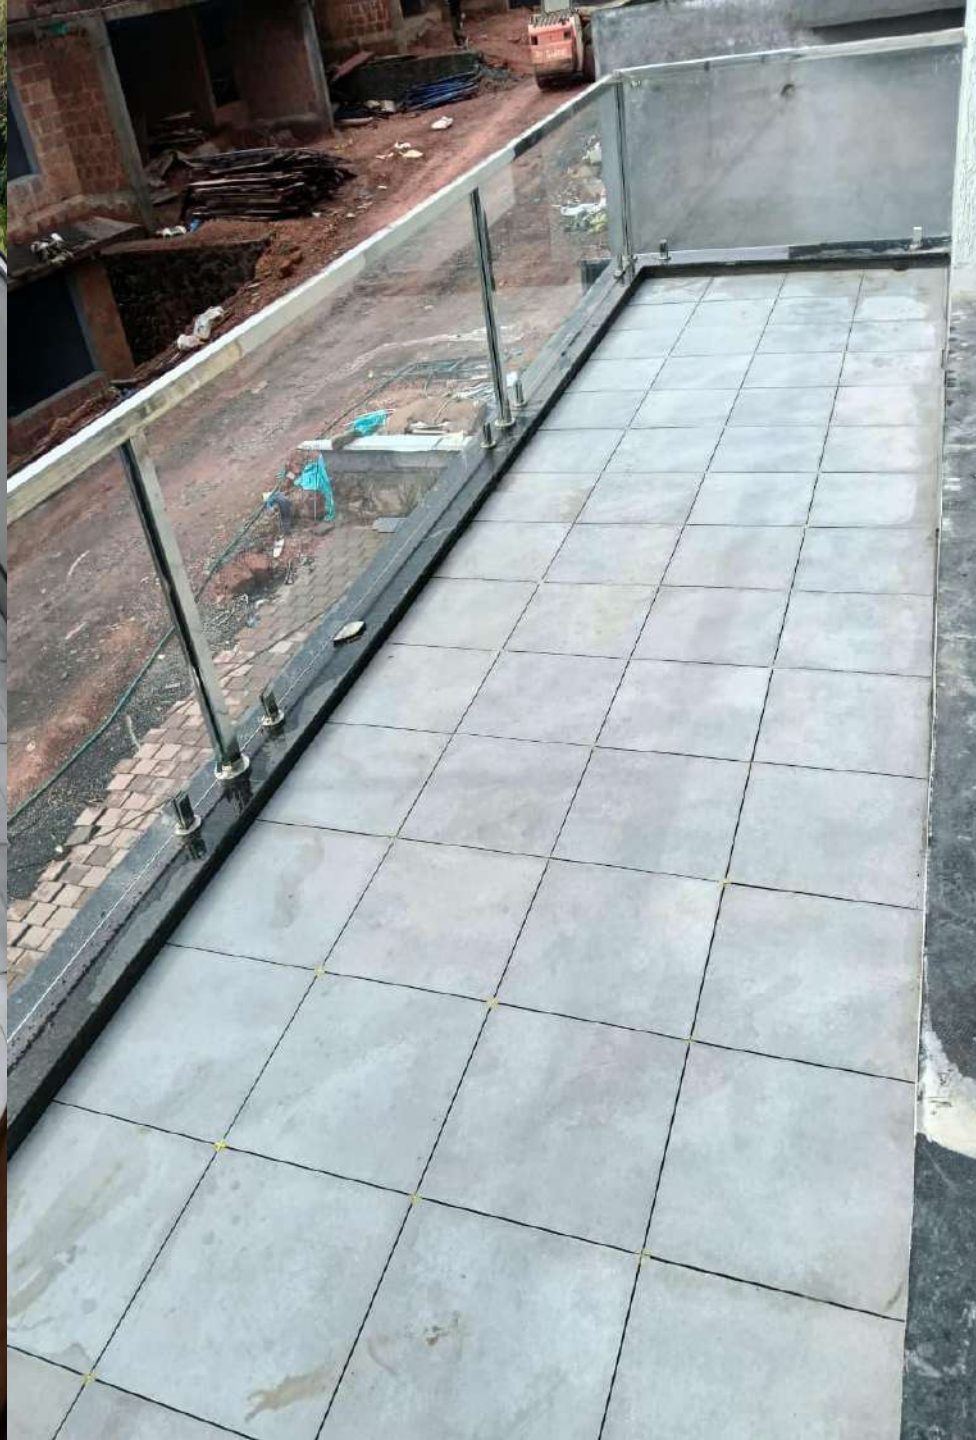

Open Terrace Tiling



Concealed Wiring



Concealed Plumbing



Painting



Mock Up Villa Interiors





Tiling



