

# SREEROSH ORCHARD

WORK PROGRESS  
NOVEMBER 2025





## WORK PROGRESS SCHEDULE - VILLA

| Sloped Roof               | 26-07-2025 | 31-10-2025 | 24-10-2025 | 24-10-2025 | 05-11-2025 | 06-11-2025 | 08-11-2025 | 10-11-2025 | 13-11-2025 | 18-11-2025 | 19-11-2025 | 17-11-2025 |  |
|---------------------------|------------|------------|------------|------------|------------|------------|------------|------------|------------|------------|------------|------------|--|
| LS above Slab/ Level      | 03-07-2025 | 18-10-2025 | 15-10-2025 | 14-10-2025 | 18-10-2025 | 22-10-2025 | 24-10-2025 | 25-10-2025 | 30-10-2025 | 30-10-2025 | 07-11-2025 | 11-11-2025 |  |
| FF Roof Slab (2nd F)      | 22-06-2025 | 06-10-2025 | 06-10-2025 | 07-10-2025 | 08-10-2025 | 09-10-2025 | 17-10-2025 | 14-10-2025 | 11-10-2025 | 14-10-2025 | 15-10-2025 | 18-10-2025 |  |
| LS Above Lintel           | 10-06-2025 | 20-08-2025 | 27-09-2025 | 27-09-2025 | 01-10-2025 | 01-10-2025 | 09-10-2025 | 02-10-2025 | 03-10-2025 | 03-10-2025 | 04-10-2025 | 04-10-2025 |  |
| Lintel Beam, Sunshade     | 08-06-2025 | 05-08-2025 | 26-08-2025 | 01-09-2025 | 03-09-2025 | 09-09-2025 | 12-09-2025 | 14-09-2025 | 17-09-2025 | 19-09-2025 | 22-09-2025 | 25-09-2025 |  |
| LS above Slab upto Lintel | 03-05-2025 | 14-07-2025 | 24-05-2025 | 23-07-2025 | 14-05-2025 | 20-08-2025 | 02-09-2025 | 31-08-2025 | 31-08-2025 | 16-08-2025 | 12-09-2025 | 15-09-2025 |  |
| GF Roof Slab (1st F)      | 28-03-2025 | 29-04-2025 | 17-04-2025 | 07-05-2025 | 09-04-2025 | 04-06-2025 | 12-06-2025 | 07-07-2025 | 19-07-2025 | 24-07-2025 | 02-08-2025 | 08-08-2025 |  |
| LS Above Lintel           | 20-03-2025 | 16-04-2025 | 01-04-2025 | 25-04-2025 | 31-03-2025 | 21-05-2025 | 30-05-2025 | 18-06-2025 | 28-06-2025 | 04-07-2025 | 13-07-2025 | 28-07-2025 |  |
| Lintel Beam, Sunshade     | 14-03-2025 | 16-04-2025 | 01-04-2025 | 21-04-2025 | 19-03-2025 | 08-05-2025 | 26-05-2025 | 29-05-2025 | 20-06-2025 | 26-06-2025 | 29-06-2025 | 15-07-2025 |  |
| Stair - upto Landing      | 14-02-2025 | 19-02-2025 | 17-02-2025 | 12-03-2025 | 10-02-2025 | 10-02-2025 | 26-02-2025 | 18-03-2025 | 17-02-2025 | 01-04-2025 | 21-04-2025 | 23-04-2025 |  |
| LS Above PB               | 22-02-2025 | 26-02-2025 | 18-02-2025 | 19-03-2025 | 08-02-2025 | 01-02-2025 | 28-02-2025 | 15-03-2025 | 19-02-2025 | 05-04-2025 | 05-04-2025 | 19-04-2025 |  |
| Earth Filling             |            |            |            |            |            |            |            |            |            |            |            |            |  |
| Plinth Beam               | 22-01-2025 | 08-02-2025 | 04-02-2025 | 26-02-2025 | 15-01-2025 | 15-01-2025 | 28-01-2025 | 19-02-2025 | 18-01-2025 | 06-03-2025 | 12-03-2025 | 18-03-2025 |  |
| Foundation / Basement     | 18-01-2025 | 05-02-2025 | 30-01-2025 | 21-02-2025 | 09-01-2025 | 10-01-2025 | 20-01-2025 | 15-01-2025 | 15-01-2025 | 01-03-2025 | 07-03-2025 | 14-03-2025 |  |
| Excavation                | 09-01-2025 | 28-01-2025 | 20-02-2025 | 08-02-2025 | 04-01-2025 | 25-12-2025 | 15-01-2025 | 01-02-2025 | 09-01-2025 | 20-02-2025 | 13-02-2025 | 06-03-2025 |  |
| RR/ LS Partition          |            | RR         | RR         | RR         | RR         | SI         | RR         | RR         | RR         | LS         | RR         | LS         |  |
|                           | VILLA # 01 | VILLA # 02 | VILLA # 03 | VILLA # 04 | VILLA # 05 | VILLA # 06 | VILLA # 07 | VILLA # 08 | VILLA # 09 | VILLA # 10 | VILLA # 11 | VILLA # 12 |  |

| INDEX       |                    |  |  |
|-------------|--------------------|--|--|
| DATE        | COMPLETED          |  |  |
| COMPLETE BY | PROGRESS           |  |  |
| DATE        | PLANNED START DATE |  |  |
|             | NOT COMMENCED      |  |  |



## WORK PROGRESS SCHEDULE - VILLA

|                             |            |            |            |            |
|-----------------------------|------------|------------|------------|------------|
| <b>Sloped Roof</b>          | 21-11-2025 | 23-11-2025 | 28-11-2025 |            |
| LS above Slab/ Level        | 11-11-2025 | 14-11-2025 | 16-11-2025 |            |
| <b>FF Roof Slab (2nd F)</b> | 17-10-2025 | 17-10-2025 | 17-10-2025 |            |
| LS Above Lintel             | 10-10-2025 | 04-10-2025 | 11-10-2025 |            |
| Lintel Beam, Sunshade       | 01-10-2025 | 28-09-2025 | 05-10-2025 |            |
| LS above Slab upto Lintel   | 23-09-2025 | 19-09-2025 | 01-10-2025 |            |
| <b>GF Roof Slab (1st F)</b> | 21-08-2025 | 22-08-2025 | 27-08-2025 |            |
| LS Above Lintel             | 15-08-2025 | 19-08-2025 | 21-08-2025 |            |
| Lintel Beam, Sunshade       | 14-08-2025 | 17-08-2025 | 19-08-2025 |            |
| Stair - upto Landing        | 08-08-2025 | 08-08-2025 | 12-08-2025 |            |
| LS Above PB                 | 05-08-2025 | 07-08-2025 | 09-08-2025 |            |
| Earth Filling               | 09-07-2025 | 16-07-2025 | 17-07-2025 |            |
| Plinth Beam                 | 06-07-2025 | 02-07-2025 | 11-07-2025 |            |
| Foundation / Basement       | 16-05-2025 | 02-05-2025 | 07-07-2025 |            |
| Excavation                  | 02-05-2025 | 24-04-2025 | 12-05-2025 |            |
| RR/ LS Partition            | RR         | RR         | RR         | RR         |
|                             | VILLA # 13 | VILLA # 14 | VILLA # 15 | VILLA # 16 |

| INDEX       |                    |  |  |
|-------------|--------------------|--|--|
| DATE        | COMPLETED          |  |  |
| COMPLETE BY | PROGRESS           |  |  |
| DATE        | PLANNED START DATE |  |  |
|             | NOT COMMENCED      |  |  |



## WORK PROGRESS SCHEDULE - VILLA

|                             |            |            |            |            |            |              |            |
|-----------------------------|------------|------------|------------|------------|------------|--------------|------------|
| <b>Sloped Roof</b>          | 12-11-2025 | 12-11-2025 | 06-11-2025 | 06-11-2025 | 04-11-2025 | 25-11-2025   | 10-10-2025 |
| LS above Slab/ Level        | 30-10-2025 | 20-10-2025 | 15-10-2025 | 16-10-2025 | 21-10-2025 | 07-11-2025   | 01-09-2025 |
| <b>FF Roof Slab (2nd F)</b> | 13-10-2025 | 13-10-2025 | 13-10-2025 | 13-10-2025 | 15-10-2025 | 18-10-2025   | 08-08-2025 |
| LS Above Lintel             | 11-10-2025 | 08-10-2025 | 07-10-2025 | 26-09-2025 | 08-10-2025 | 16-10-2025   | 25-07-2025 |
| Lintel Beam, Sunshade       | 07-10-2025 | 29-09-2025 | 23-09-2025 | 15-09-2025 | 12-09-2025 | 14-10-2025   | 20-07-2025 |
| LS above Slab upto Lintel   | 25-09-2025 | 16-09-2025 | 16-09-2025 | 04-09-2025 | 04-09-2025 | 09-10-2025   | 15-07-2025 |
| <b>GF Roof Slab (1st F)</b> | 18-08-2025 | 12-08-2025 | 08-08-2025 | 03-08-2025 | 14-06-2025 | 09-04-2025   | 01-04-2025 |
| LS Above Lintel             | 15-08-2025 | 07-08-2025 | 02-08-2025 | 29-07-2025 | 11-05-2025 | 20-03-2025   | 08-03-2025 |
| Lintel Beam, Sunshade       | 13-08-2025 | 05-08-2025 | 30-07-2025 | 26-07-2025 | 21-04-2025 | 14-03-2025   | 01-03-2025 |
| Stair - upto Landing        | 05-08-2025 | 31-07-2025 | 18-07-2025 | 29-06-2025 | 29-05-2025 | no RCC stair | 01-03-2025 |
| LS Above PB                 | 04-08-2025 | 04-05-2025 | 12-04-2025 | 21-03-2025 | 23-01-2025 | 30-01-2025   | 24-01-2025 |
| Earth Filling               | 09-07-2025 |            |            |            |            |              |            |
| Plinth Beam                 | 31-05-2025 | 15-04-2025 | 26-03-2025 | 11-03-2025 | 20-01-2025 | 16-01-2025   | 13-01-2025 |
| Foundation / Basement       | 09-05-2025 | 02-04-2025 | 19-03-2025 | 07-03-2025 | 10-01-2025 | 06-01-2025   | 30-12-2024 |
| Excavation                  | 25-04-2025 | 27-03-2025 | 13-03-2025 | 03-03-2025 | 04-01-2025 | 30-12-2025   | 26-12-2024 |
| RR/ LS Partition            | LS         | LS         | LS         | LS         | RR         | RR           | LS         |
|                             | VILLA # 16 | VILLA # 17 | VILLA # 18 | VILLA # 19 | VILLA # 25 | VILLA # 26   | VILLA # 27 |

| INDEX       |                    |
|-------------|--------------------|
| DATE        | COMPLETED          |
| COMPLETE BY | PROGRESS           |
| DATE        | PLANNED START DATE |
|             | NOT COMMENCED      |



## WORK PROGRESS SCHEDULE - VILLA


| <b>Sloped Roof</b>          | 28-10-2025 | 14-11-2025 | 19-11-2025 | 08-11-2025 |    | 18-11-2025 | 07-11-2025 | 22-11-2025 | 04-11-2025 | 22-11-2025 | 05-11-2025 | 24-11-2025 |    |
|-----------------------------|------------|------------|------------|------------|----|------------|------------|------------|------------|------------|------------|------------|----|
| LS above Slab/ Level        | 25-09-2025 | 09-11-2025 | 13-11-2025 | 29-10-2025 |    | 24-10-2025 | 24-10-2025 | 05-11-2025 | 14-10-2025 | 01-11-2025 | 28-10-2025 | 10-11-2025 |    |
| <b>FF Roof Slab (2nd F)</b> | 08-09-2025 | 07-10-2025 | 16-10-2025 | 16-10-2025 |    | 18-10-2025 | 17-10-2025 | 17-10-2025 | 09-10-2025 | 17-10-2025 | 15-10-2025 | 15-10-2025 |    |
| LS Above Lintel             | 02-09-2025 | 19-09-2025 | 25-09-2025 | 27-09-2025 |    | 07-10-2025 | 02-10-2025 | 02-10-2025 | 02-10-2025 | 02-10-2025 | 12-10-2025 | 13-10-2025 |    |
| Lintel Beam, Sunshade       | 25-08-2025 | 31-08-2025 | 27-08-2025 | 19-09-2025 |    | 08-09-2025 | 09-09-2025 | 02-09-2025 | 25-09-2025 | 16-09-2025 | 08-10-2025 | 03-10-2025 |    |
| LS above Slab upto Lintel   | 05-05-2025 | 27-08-2025 | 20-08-2025 | 10-09-2025 |    | 22-08-2025 | 30-08-2025 | 27-08-2025 | 19-09-2025 | 11-09-2025 | 23-09-2025 | 24-09-2025 |    |
| <b>GF Roof Slab (1st F)</b> | 22-03-2025 | 30-04-2025 | 23-06-2025 | 17-07-2025 |    | 23-07-2025 | 11-07-2025 | 17-05-2025 | 04-08-2025 | 29-07-2025 | 17-08-2025 | 19-08-2025 |    |
| LS Above Lintel             | 01-03-2025 | 08-04-2025 | 04-06-2025 | 07-07-2025 |    | 10-07-2025 | 29-06-2025 | 11-05-2025 | 24-07-2025 | 16-07-2025 | 13-08-2025 | 16-08-2025 |    |
| Lintel Beam, Sunshade       | 22-02-2025 | 29-03-2025 | 21-05-2025 | 27-06-2025 |    | 30-06-2025 | 20-06-2025 | 25-04-2025 | 24-07-2025 | 04-07-2025 | 11-08-2025 | 15-08-2025 |    |
| Stair - upto Landing        | 22-02-2025 | 29-03-2025 | 05-05-2025 | 09-06-2025 |    | 12-06-2025 | 28-05-2025 | 07-04-2025 | 14-06-2025 | 15-06-2025 | 21-06-2025 | 06-08-2025 |    |
| LS Above PB                 | 18-01-2025 | 07-02-2025 | 07-02-2025 | 01-03-2025 |    | 12-03-2025 | 08-02-2025 | 28-02-2025 | 03-03-2025 | 08-02-2025 | 21-02-2025 | 12-02-2025 |    |
| Earth Filling               |            |            |            |            |    |            |            |            |            |            |            |            |    |
| Plinth Beam                 | 09-01-2025 | 22-01-2025 | 24-01-2025 | 17-02-2025 |    | 03-03-2025 | 31-01-2025 | 21-02-2025 | 25-02-2025 | 28-01-2025 | 10-02-2025 | 06-02-2025 |    |
| Foundation                  | 05-01-2025 | 17-01-2025 | 10-01-2025 | 13-02-2025 |    | 21-02-2025 | 30-01-2025 | 14-02-2025 | 20-02-2025 | 22-01-2025 | 07-02-2025 | 31-01-2025 |    |
| Excavation                  | 25-12-2024 | 12-01-2025 | 06-01-2025 | 31-01-2025 |    | 16-02-2025 | 24-01-2025 | 09-02-2025 | 13-02-2025 | 16-01-2025 | 02-02-2025 | 26-01-2025 |    |
| RR/ LS Partition            | LS         | RR         | RR         | RR         | RR | RR         | RR         | RR         | LS         | RR         | RR         | LS         | RR |
|                             | VILLA # 28 | VILLA # 29 | VILLA # 30 | VILLA # 31 |    | VILLA # 32 | VILLA # 33 | VILLA # 34 | VILLA # 35 | VILLA # 36 | VILLA # 37 | VILLA # 38 |    |

| INDEX       |                    |
|-------------|--------------------|
| DATE        | COMPLETED          |
| COMPLETE BY | PROGRESS           |
| DATE        | PLANNED START DATE |
|             | NOT COMMENCED      |

## WORK PROGRESS SCHEDULE - VILLA (#20 up to 25)

|                             |            |                          |            |            |                          |            |            |
|-----------------------------|------------|--------------------------|------------|------------|--------------------------|------------|------------|
| <b>Sloped Roof</b>          |            |                          |            |            |                          |            |            |
| LS above Slab/ Level        |            |                          |            |            |                          |            |            |
| <b>FF Roof Slab (2nd F)</b> |            |                          |            |            |                          |            |            |
| LS Above Lintel             |            |                          |            |            |                          |            |            |
| Lintel Beam, Sunshade       |            |                          |            |            |                          |            |            |
| LS above Slab upto Lintel   |            |                          |            |            |                          |            |            |
| <b>GF Roof Slab (1st F)</b> |            |                          |            |            |                          |            |            |
| LS Above Lintel             |            |                          |            |            |                          |            |            |
| Lintel Beam, Sunshade       |            |                          |            |            |                          |            |            |
| Stair - upto Landing        |            |                          |            |            |                          |            |            |
| LS Above PB                 |            |                          |            |            |                          |            |            |
| Earth Filling               |            |                          |            |            |                          |            |            |
| Plinth Beam                 |            |                          |            |            |                          |            |            |
| Foundation / Basement       |            |                          |            |            |                          |            |            |
| Excavation                  |            |                          |            |            |                          |            |            |
| RR/ LS Partition            | RR         | RR                       |            | LS         | RR                       | RR         | LS         |
|                             | VILLA # 20 | VILLA # 23<br>VILLA # 22 | VILLA # 23 | VILLA # 24 | VILLA # 25<br>VILLA # 20 | VILLA # 21 | VILLA # 22 |
|                             | RR         |                          | RR         |            | RR                       |            |            |
|                             | VILLA # 19 |                          | VILLA # 25 |            | VILLA # 20               |            |            |

| INDEX |                           |
|-------|---------------------------|
| DATE  | COMPLETED                 |
|       | PROGRESS                  |
| DATE  | PLANNED START DATE        |
|       | NOT COMMENCED             |
|       | SCOPE OF KRISHNA BUILDERS |

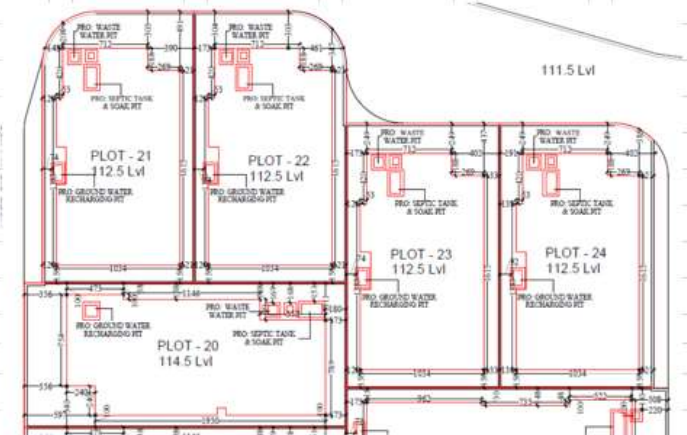



## WORK PROGRESS SCHEDULE - CLUB HOUSE

|  |                 |
|--|-----------------|
|  | PROGRESS        |
|  | NOT APPLICABLE  |
|  | COMPLETED       |
|  | NOT COMMENCED   |
|  | UPTO -660 LEVEL |

## WORK PROGRESS SCHEDULE - MISC

|            | Anti Termite | Floor PCC  | Button Marking - Internal | Electrical - Chasing - Internal | Electrical - BOX & Conduits - Internal | Plastering - Internal | Plumbing Chasing & Concealed Works | Button Marking - External | Electrical - Chasing - External | Electrical - Box & Conduits - External | Plastering - External | Water Proofing - Box Works | Ledge Wall in Toilets | Water Proofing Toilets | Screed Works - Toilets |
|------------|--------------|------------|---------------------------|---------------------------------|----------------------------------------|-----------------------|------------------------------------|---------------------------|---------------------------------|----------------------------------------|-----------------------|----------------------------|-----------------------|------------------------|------------------------|
| Villa # 01 | 24-06-2025   | 24-06-2025 | 06-08-2025                | 20-08-2025                      | 25-08-2025                             | 30-08-2025            |                                    | 30-08-2025                | 02-09-2025                      | 30-09-2025                             | box                   |                            |                       |                        |                        |
| Villa # 02 | 06-10-2025   | 07-10-2025 | 06-08-2025                | 11-11-2025                      | 17-11-2025                             |                       |                                    |                           |                                 |                                        | box                   |                            |                       |                        |                        |
| Villa # 03 | 06-10-2025   | 08-10-2025 | 06-08-2025                |                                 |                                        |                       |                                    |                           |                                 |                                        | box                   |                            |                       |                        |                        |
| Villa # 04 | 08-10-2025   | 09-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        | box                   |                            |                       |                        |                        |
| Villa # 05 | 10-10-2025   | 11-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        | box                   |                            |                       |                        |                        |
| Villa # 06 | 16-10-2025   | 17-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        | box                   |                            |                       |                        |                        |
| Villa # 07 | 16-10-2025   | 17-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        | box                   |                            |                       |                        |                        |
| Villa # 08 | 03-11-2025   | 04-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 09 | 29-10-2025   | 30-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 10 | 28-10-2025   | 30-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 11 | 28-10-2025   | 29-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 12 | 22-10-2025   | 23-10-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 13 | 07-11-2025   | 08-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 14 | 20-11-2025   |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 15 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 21 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 22 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |

| INDEX       |                    |  |
|-------------|--------------------|--|
| DATE        | COMPLETED          |  |
| COMPLETE BY | PROGRESS           |  |
| DATE        | PLANNED START DATE |  |
|             | NOT COMMENCED      |  |



## WORK PROGRESS SCHEDULE - MISC

|            | Anti Termite | Floor PCC  | Button Marking - Internal | Electrical - Chasing - Internal | Electrical - BOX & Conduits - Internal | Plastering - Internal | Plumbing Chasing & Concealed Works | Button Marking - External | Electrical - Chasing - External | Electrical - Box & Conduits - External | Plastering - External | Water Proofing - Box Works | Ledge Wall in Toilets | Water Proofing Toilets | Screed Works - Toilets |
|------------|--------------|------------|---------------------------|---------------------------------|----------------------------------------|-----------------------|------------------------------------|---------------------------|---------------------------------|----------------------------------------|-----------------------|----------------------------|-----------------------|------------------------|------------------------|
| Villa # 16 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 17 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 18 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 19 | 05-11-2025   | 06-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 20 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 23 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 24 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 25 | 03-11-2025   | 04-11-2025 | 20-11-2025                |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 26 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 27 | 22-10-2025   | 23-10-2025 | 13-11-2025                | 17-11-2025                      | 23-11-2025                             |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 28 | 28-10-2025   | 29-10-2025 | 18-11-2025                |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 29 | 08-11-2025   | 09-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 30 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 31 | 11-11-2025   |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 32 | 08-11-2025   | 09-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 33 | 01-11-2025   | 02-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 34 | 01-11-2025   | 02-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 35 | 01-11-2025   |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 36 | 04-11-2025   | 05-11-2025 |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 37 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |
| Villa # 38 |              |            |                           |                                 |                                        |                       |                                    |                           |                                 |                                        |                       |                            |                       |                        |                        |

| INDEX       |                    |  |  |
|-------------|--------------------|--|--|
| DATE        | COMPLETED          |  |  |
| COMPLETE BY | PROGRESS           |  |  |
| DATE        | PLANNED START DATE |  |  |
|             | NOT COMMENCED      |  |  |



VILLA # 01





VILLA # 02





VILLA # 03





VILLA # 04





VILLA # 05





VILLA # 06





VILLA # 07





VILLA # 08





VILLA # 09





VILLA # 10





VILLA # 11





VILLA # 12





VILLA # 13





VILLA # 14





VILLA # 15





VILLA # 16





VILLA # 17





VILLA # 18



VILLA # 19





VILLA # 20 UP TO  
VILLA # 25 - PROGRESS





VILLA # 25





VILLA # 26





VILLA # 27





VILLA # 28





VILLA # 29





VILLA # 30





VILLA # 31





VILLA # 32





VILLA # 33





VILLA # 34





VILLA # 35





VILLA # 36





VILLA # 37





VILLA # 38





CLUB HOUSE





CLUB HOUSE



























































